



Upper Rio Grande Flood Control Projects

International Boundary and Water Commission
United States Section
Engineering Services Division

April 17, 2013



International Boundary and Water Commission United States Section


CURRENT AREA LEVEE PROJECTS

- Mesilla Levee Improvements, Phase 2
- Sunland Park Levee Improvements
- Vado Levee Design
- Canutillo Levee Design, Phase 2
- Courchesne & NEMEXAS Levee Design
- American Canal Re-Lining Design



International Boundary and Water Commission United States Section


CANALIZATION PROJECTS

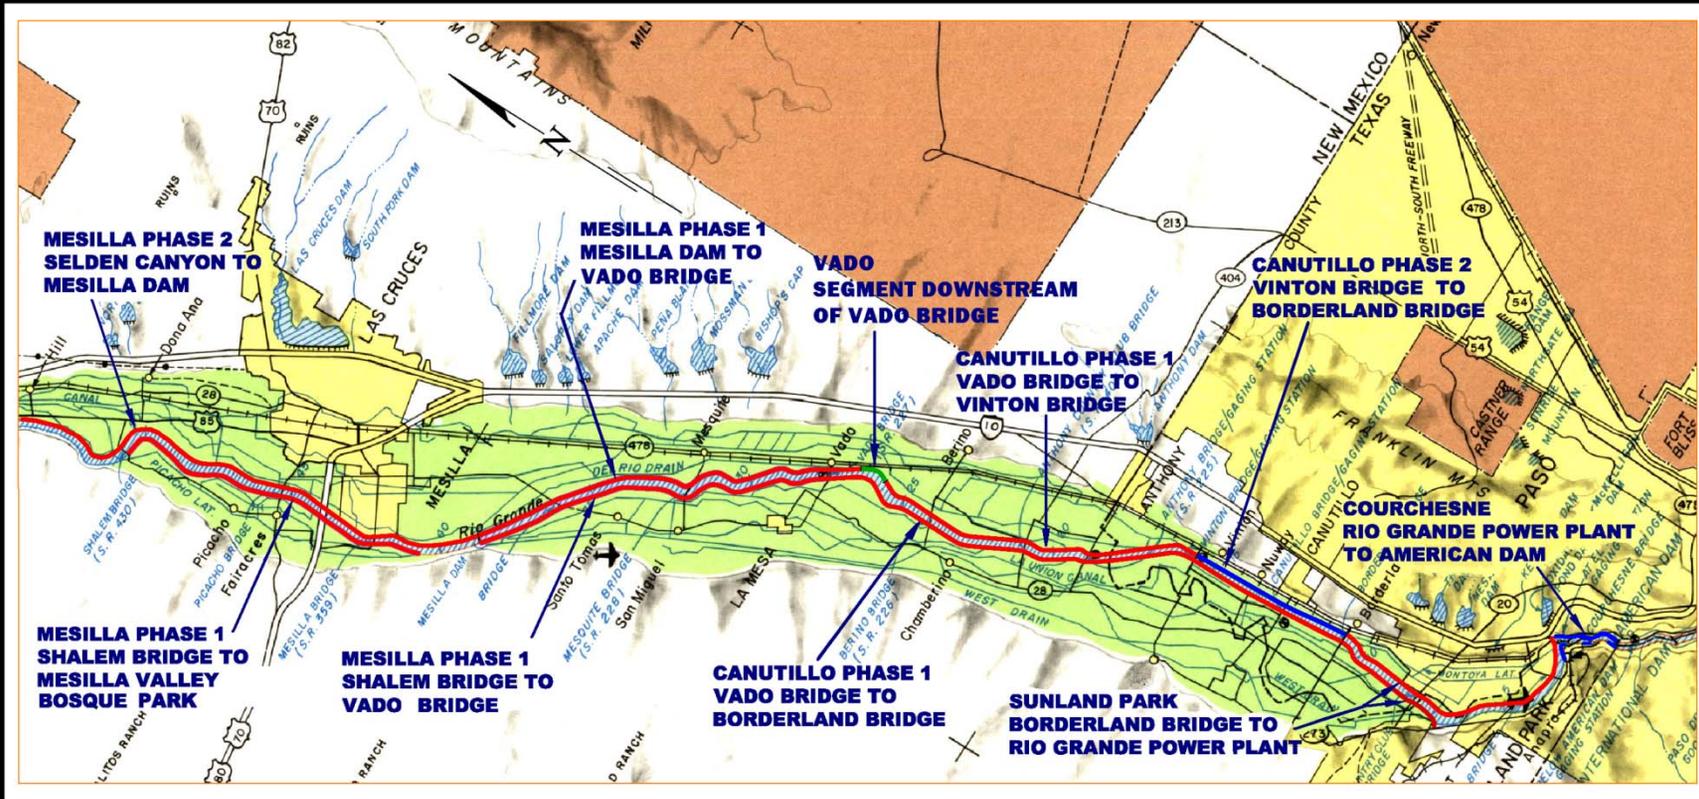



International Boundary and Water Commission United States Section

MESILLA PHASE 2

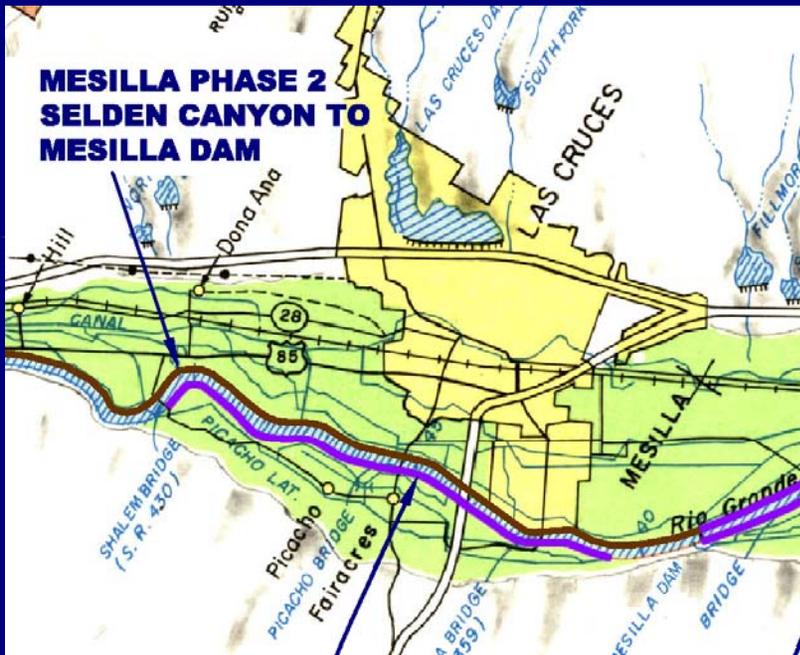


Mesilla Phase 2 – Brown Line
Leasburg to Mesilla Dam
(east levee)

- 19.6 miles of levee
- \$17.1 million contract to Briston Construction LLC
- Notice to Proceed issued September 25, 2010
- Anticipated completion September 2013
- 16.1 miles of embankment complete – 85%



International Boundary and Water Commission United States Section

SUNLAND PARK

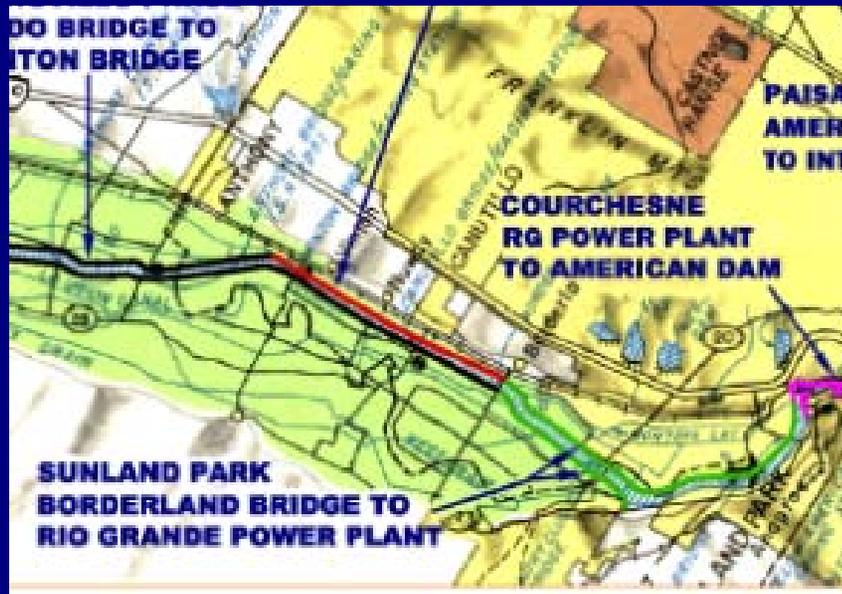

Sunland Park – Green Line
Borderland Bridge To Power Plant
(east and west levees)

- 11.8 miles of levee
- \$9.2 million awarded to Ultimate Concrete LLC
- Notice to Proceed issued September 28, 2010
- Anticipated completion November 2012
- 11.8 miles of embankment complete



International Boundary and Water Commission United States Section

VADO LEVEE DESIGN



Vado – Orange Line
(east levee)

- Design - 1.1 miles of levee
- \$0.61 million awarded to Tetra Tech, Inc.
- Design complete
- Construction estimated in late-2013



International Boundary and Water Commission United States Section

CANUTILLO PHASE 2 DESIGN



Canutillo Phase 2 – Red Line
Vinton Bridge to Borderland Bridge
(east levee)

- Design - 5.7 miles of levee
- \$1.8 million design contract awarded to URS Group, Inc.
- Notice to Proceed issued on June 17, 2010
- Anticipated completion to be determined
- 90% design complete
- Construction estimated in 2014 through 2017



International Boundary and Water Commission United States Section

AMERICAN CANAL RE-LINING DESIGN



American Canal – Red Line

- Design - 1.6 miles of canal
- \$2.3 million design contract awarded to URS Group, Inc.
- Notice to Proceed issued September 6, 2011
- Anticipated completion to be determined
- 90% design complete
- Construction estimated in 2014 or 2015



International Boundary and Water Commission

United States Section

Engineering Services Division

Construction Branch

4171 N. Mesa, Ste C-100

El Paso, TX 79902

(915) 832-4759

Andrea Glover, PE

(915) 832-4747
