



Upper Rio Grande Flood Control Projects

International Boundary and Water Commission
United States Section
Engineering Services Division

July 19, 2012



International Boundary and Water Commission

United States Section


CURRENT AREA LEVEE PROJECTS

- Mesilla Levee Improvements, Phase 1
- Mesilla Levee Improvements, Phase 2
- Canutillo Levee Improvements
- Sunland Park Levee Improvements
- Vado Levee Design
- Canutillo Levee Design, Phase 2
- Courchesne & NEMEXAS Levee Design
- American Canal Re-Lining Design
- Yselta to Fabens Levee Improvements



International Boundary and Water Commission United States Section


CANALIZATION PROJECTS

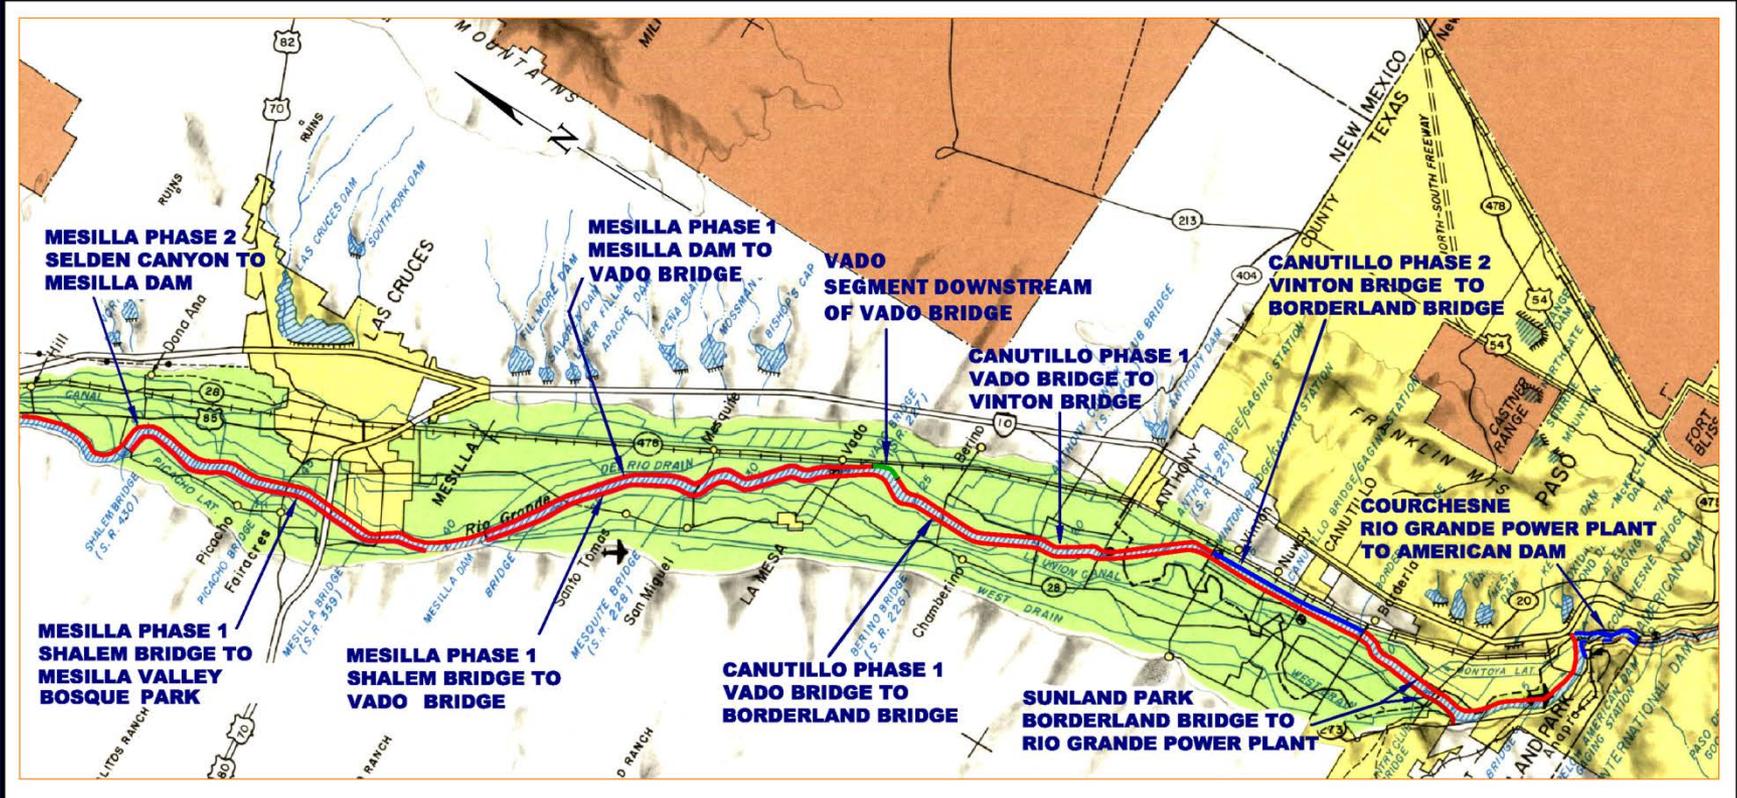



International Boundary and Water Commission United States Section

MESILLA PHASE 1

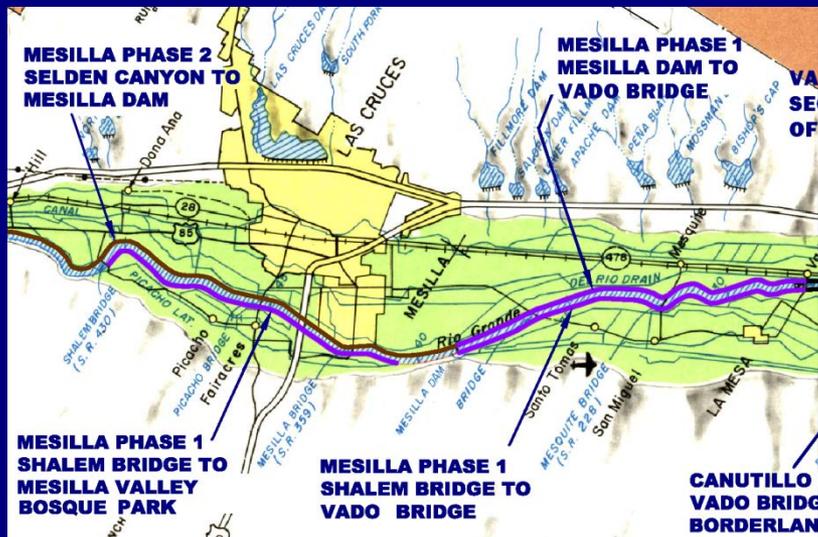


Mesilla Phase 1 – Purple Line
Shalem Colony Bridge to Mesilla Dam
(west levee)
Mesilla Dam to Vado Bridge
(east and west levee)

- 33.4 miles of levee
- \$31.1 million contract to Lakeshore Engineering Services, Inc.
- Notice to Proceed issued January 25, 2010
- Construction complete
- Minor punch list items remain



International Boundary and Water Commission United States Section

MESILLA PHASE 2

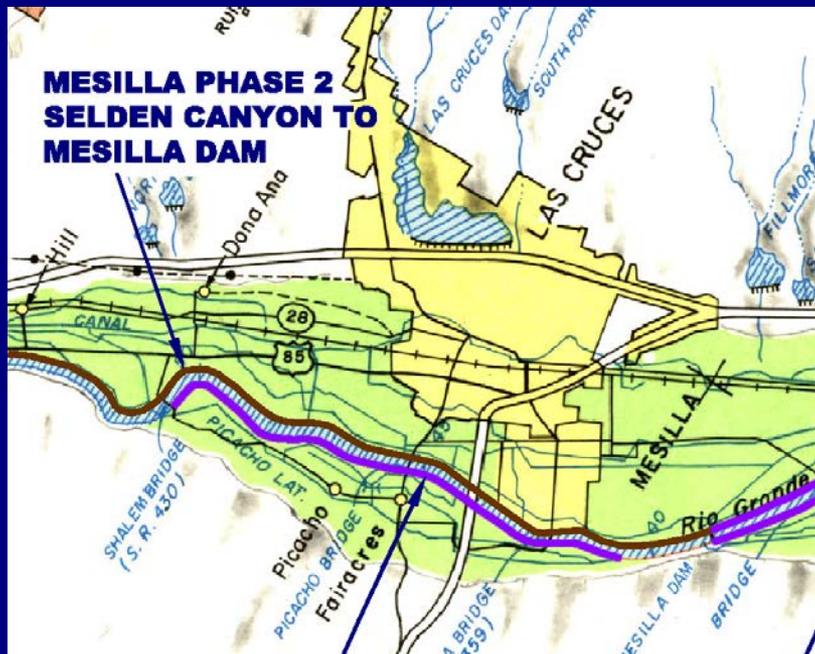


Mesilla Phase 2 – Brown Line
Leasburg to Mesilla Dam
(east levee)

- 19.6 miles of levee
- \$14.8 million contract to Briston Construction LLC
- Notice to Proceed issued September 25, 2010
- Anticipated completion December 2012
- 14.7 miles of embankment complete – 75%



International Boundary and Water Commission United States Section

CANUTILLO PHASE 1

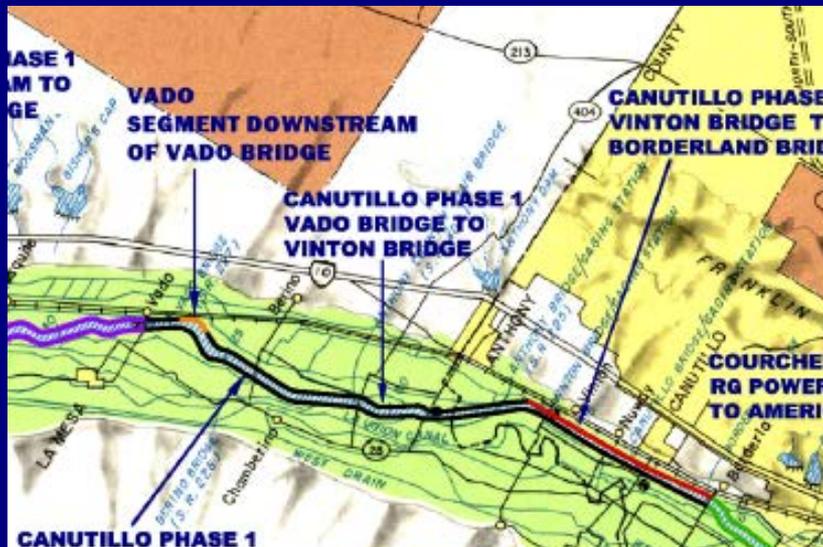


Canutillo 1 – Black Line
Vado Bridge To Vinton Bridge
(east and west levees)
Vinton Bridge to Borderland Bridge
(west levee)

- 28.6 levee miles
- \$19.3 million contract to Milestone Excavation, Inc.
- Notice to Proceed issued February 3, 2010
- Anticipated completion June 2012
- Construction complete



International Boundary and Water Commission United States Section

SUNLAND PARK

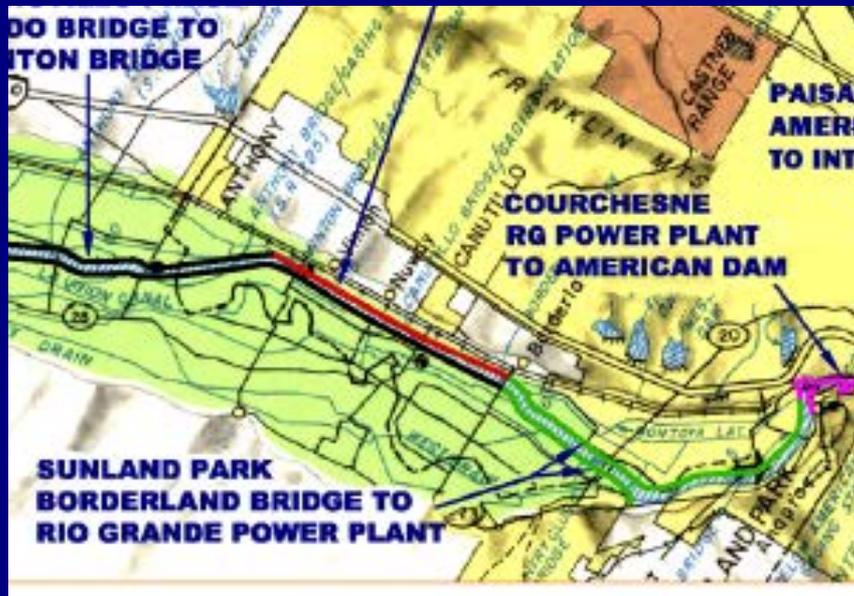

Sunland Park – Green Line
Borderland Bridge To Power Plant
(east and west levees)

- 11.8 miles of levee
- \$9.2 million awarded to Ultimate Concrete LLC
- Notice to Proceed issued September 28, 2010
- Anticipated completion August 2012
- 7.3 miles of embankment complete – 70%



International Boundary and Water Commission United States Section

VADO LEVELLE DESIGN




Vado – Orange Line
(east levee)

- Design - 1.1 miles of levee
- \$0.61 million awarded to Tetra Tech, Inc.
- Design complete
- Construction estimated in 2013



International Boundary and Water Commission United States Section

CANUTILLO PHASE 2 DESIGN

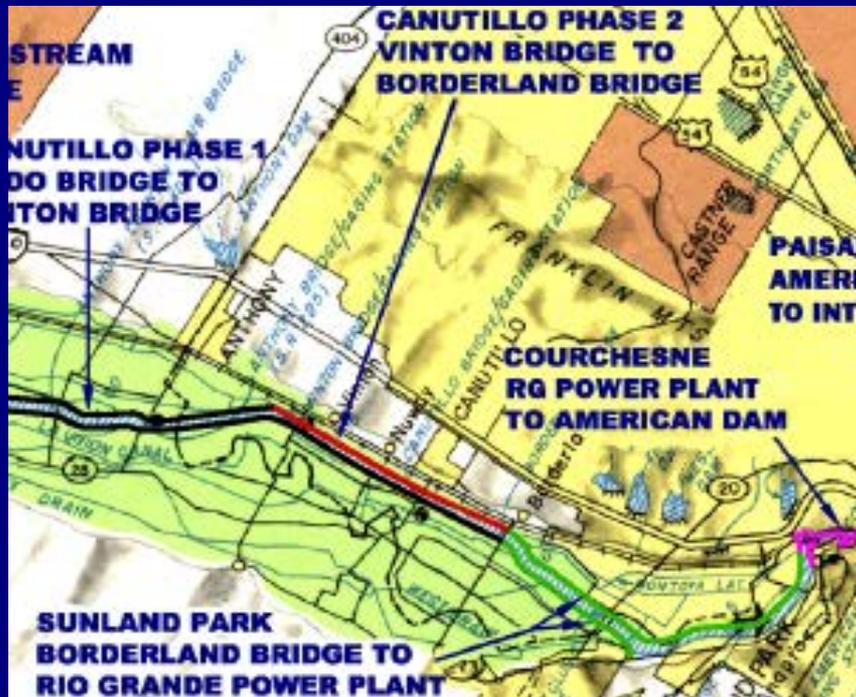


Canutillo Phase 2 – Red Line
Vinton Bridge to Borderland Bridge
(east levee)

- Design - 5.7 miles of levee
- \$1.8 million design contract awarded to URS Group, Inc.
- Notice to Proceed issued on June 17, 2010
- Anticipated completion to be determined
- 90% design complete
- Construction estimated in 2014 through 2017



International Boundary and Water Commission United States Section

COURCHESNE & NEMEXAS REACH DESIGNS

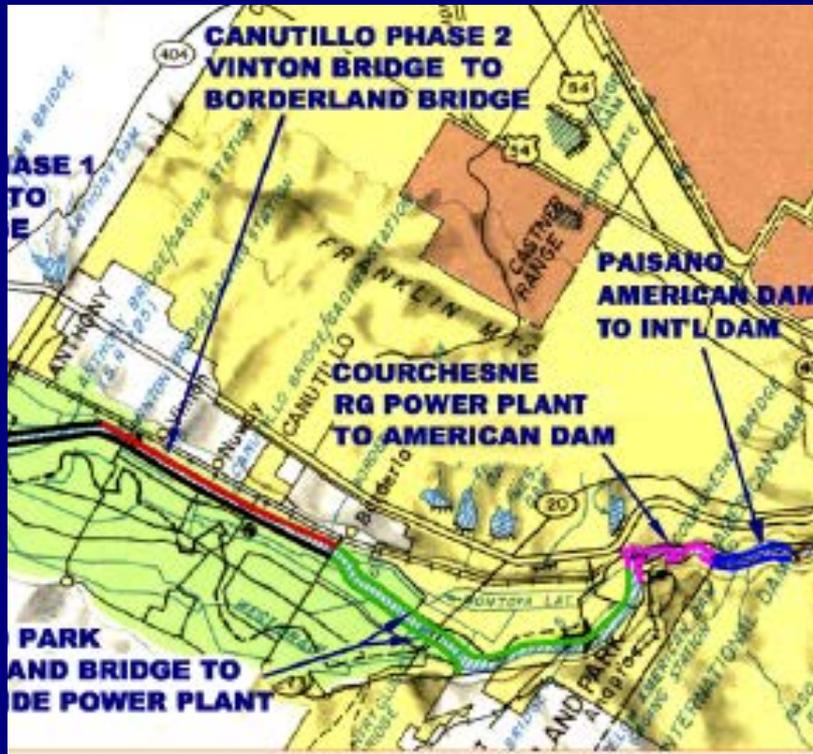

Courchesne – Pink Line
(east levee)

- Design - 3.8 miles of levee
- \$1.2 million design contract awarded to URS Group, Inc.
- Notice to Proceed issued September 17, 2010
- Anticipated completion to be determined
- 60% design complete
- Construction estimated in 2018 through 2020



International Boundary and Water Commission United States Section

AMERICAN CANAL RE-LINING DESIGN



American Canal – Red Line

- Design - miles of canal
- million design contract awarded to URS Group, Inc.
- Notice to Proceed issued
- Anticipated completion to be determined
- 60% design complete
- Construction estimated in 2013 or 2014



International Boundary and Water Commission United States Section

YSLETA TO FABENS



Socorro, TX to Fabens, TX – Pink Line
Ysleta Bridge to Fabens

- Design - 15.7 miles of levee
- \$1.8 million design contract awarded to URS Group, Inc.
- Design Complete
- Construction expected to be awarded in 2012.
Solicitation announcement is on FedBizOps.



International Boundary and Water Commission

United States Section

Engineering Services Division

Construction Branch

4171 N. Mesa, Ste C-100

El Paso, TX 79902

(915) 832-4759

Andrea Glover, PE

(915) 832-4747
